


GraniteFallsBr102Replacement (RC1622) 270-Day ENVS version - Biological Assessment - "Letter of No Effect" (No Formal Consultation Required)

ID	Proj. Task	% Complete	Dur.	Sch. Start	Sch. Fin.(ECD)	Total Slack	Act. Start	Act. Fin.	'13	'14	'15	2014	'17	'18	'19	'20	2019	'22
0	GraniteFallsBr102Replacement (RC1622) 270-Day ENVS version - Biological Assessment - "Letter of No Effect" (No Formal Consultation Required)	5%	1785 days	10/13/14	11/5/21	0 days	10/13/14	NA										5%
1	STRUCTURAL FINAL DESIGN PHASE - (FROM 30% TO 100% PSE SUBMITTAL)	0%	422 days	10/10/17	6/18/19	-259 days	NA	NA										0%
20	ENVIRONMENTAL PERMITTING PHASE	0%	375 days	10/10/17	4/11/19	-212 days	NA	NA										0%
35	RIGHT OF WAY PHASE	33%	753 days	10/13/14	10/17/17	107 days	10/13/14	NA										33%
41	CIVIL - FINAL DESIGN PHASE - (FROM 30% TO 100% PSE SUBMITTAL)	0%	393 days	10/10/17	5/7/19	-230 days	NA	NA										0%
74	OBLIGATE TIGER FUNDS	0%	50 days	6/19/19	8/28/19	-259 days	NA	NA										0%
75	ADVERTISEMENT PHASE	0%	72 days	8/29/19	12/13/19	-259 days	NA	NA										0%
76	AD DATE (QPR: Advertisement)	0%	0 days	9/12/19	9/12/19	-268 days	NA	NA										0%
77	Bid Period ending at Bid Opening	0%	22 days	9/12/19	10/11/19	473 days	NA	NA										0%
78	PE/CE Transition, Contract Execution and Notice to Proceed	0%	36 days	8/29/19	10/21/19	0 days	NA	NA										0%
79	CONSTRUCTION BID AWARD	0%	1 day	12/13/19	12/13/19	473 days	NA	NA										0%
80	CONSTRUCTION PHASE	0%	530 days	10/22/19	11/5/21	0 days	NA	NA										0%
81	Start Construction	0%	1 day	1/14/20	1/14/20	473 days	NA	NA										0%

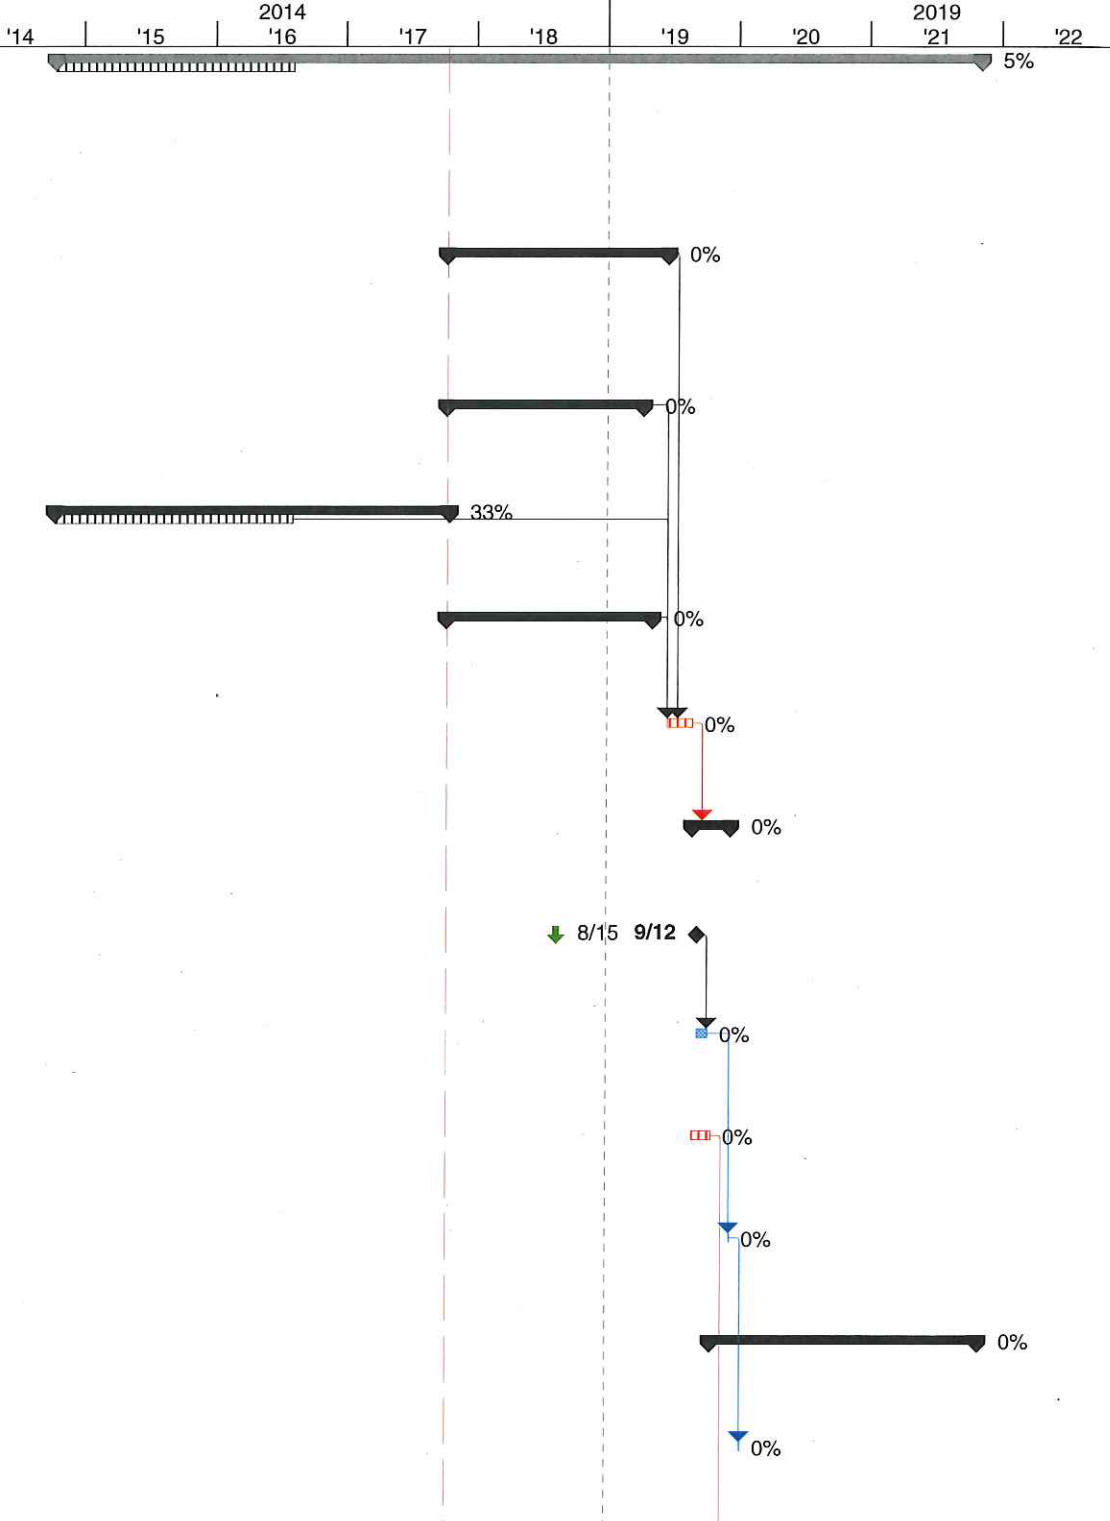

Critical		Task Progress		Summary Progress		Task		Duration-only		Critical Progress	
Critical Split		Baseline		Summary		Inactive Task		Manual Summary Rollup			
Critical Progress		Baseline Split		External Tasks		Inactive Milestone		Manual Summary			
Task		Baseline Milestone		Project Summary		Inactive Summary		Start-only			
Split		Milestone		Critical Split		Manual Task		Finish-only			
